ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	Project Requirements	2 days	Fri 21-04-17	Mon 24-04-17		Technical Leader
2	Initial Requirement	3 days	Tue 25-04-17	Thu 27-04-17	1	Technical Leader,Project Manager
3	Detailled Requirement	5 days	Fri 28-04-17	Thu 04-05-17	2	Technical Leader,,Project Manager,Testi
4	Business Planning	3 days	Fri 05-05-17	Tue 09-05-17	3	Project Manager,Web Designer
5	Business Launch Design	4.5 days	Wed 10-05-17	Tue 16-05-17	4	Project Manager,Technical Leader
6	Product Design	6 days	Wed 10-05-17	Wed 17-05-17	4	Software Developer
7	Installment	2 days	Thu 18-05-17	Fri 19-05-17	5,6	Research manager,Sponsor
8	Working Sector Define	1.5 days	Mon 22-05-17	Tue 23-05-17	7	Project Manager,worker
9	Research and Devlopment	5 days	Mon 22-05-17	Fri 26-05-17	7	
10	Productivity Define	3.33 days	Mon 29-05-17	Thu 01-06-17	8,9	programmer,Sponsor,worker
11	Testing	4 days	Thu 01-06-17	Wed 07-06-17	10	Testing Enginner
12	Resource incresment	3 days	Wed 07-06-17	Mon 12-06-17	11	Sponsor,Project Manager
13	Finish	0 days	Mon 12-06-17	Mon 12-06-17	12	programmer,Project Manager,Research

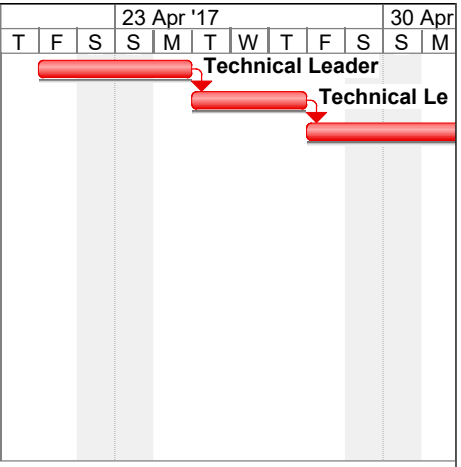

Project: Software Developmet
Date: Wed 23-08-17

Task	Rolled Up Task	External Tasks	
Critical Task	Rolled Up Critical Task	Project Summary	
Progress	Rolled Up Milestone	Group By Summary	
Milestone	Rolled Up Progress	Deadline	
Summary	Split		

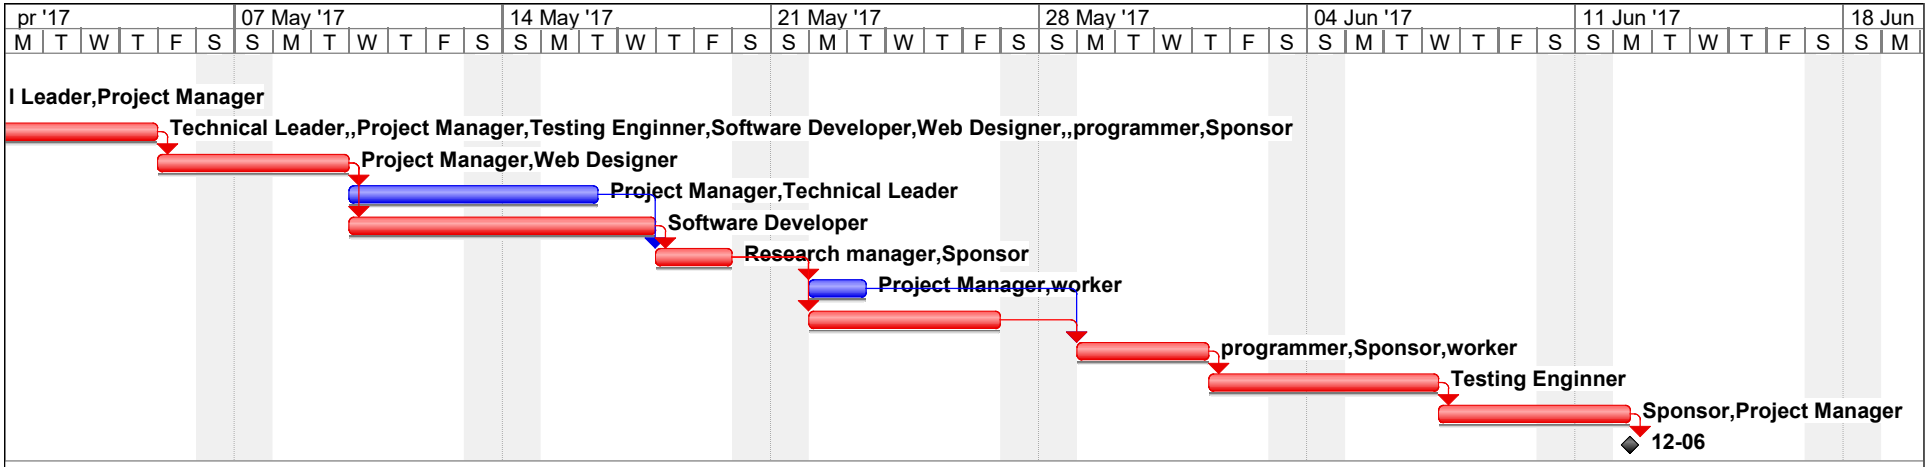

Project: Software Developmet
Date: Wed 23-08-17

Task		Rolled Up Task		External Tasks	
Critical Task		Rolled Up Critical Task		Project Summary	
Progress		Rolled Up Milestone	◇	Group By Summary	
Milestone	◆	Rolled Up Progress		Deadline	⇩
Summary		Split			
